

MARTIN'S PARK: CONSTRUCTION UPDATE- November 16, 2018

This Martin's Park update will fill you in what has been happening on site since the October 3rd update and what to look forward to in the next 2-3 weeks..

What has been done in the last month:

- The biggest visual impact on the site in the last month is the beginning of the geofoam installation. This really begins to show the topography of the finished park. The geofoam on the north side of the park is installed.
- The north and south walls along the harborwalk have been poured.
- The mudmat on the north side has been poured to support the geofoam.
- The foundation was poured for the net climber.
- The foundation was poured for the radius wall.
- The amphitheater foundation was also poured.

Here is what to look for in the next 2-3 weeks:

On the north side of the park (closest to Seaport Blvd.):

- The installed geofoam will be wrapped in filter fabric.
- The soils will begin to be placed.
- Tree planting will begin as weather permits.

On the south side of the park (closest to the Children's Museum):

- The amphitheater structure will continue to be installed.
- The radius wall surrounding the net climber will be poured.
- The mud slab under the south geofoam will be poured.
- Geofoam installation on the south side will begin.

General park:

- Granite deliveries will begin.
- Stone will begin to be placed on site at the bridge abutments.

As always, please feel free to reach out for any questions or comments.
Lauren.Bryant@boston.gov




North geofoam installation





North Harborwalk wall poured

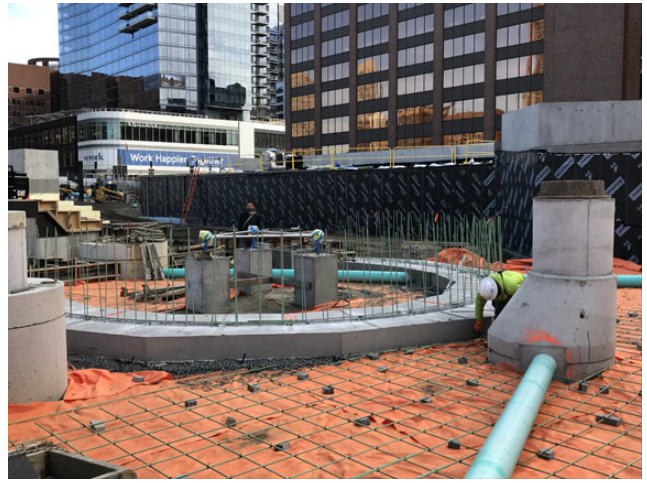

Foundation for radius wall



Foundation for net climber



South site prepped for mud slab to be poured



Amphitheater foundation installation
